VHERNIER MIAMI AT DESIGN DISTRICT
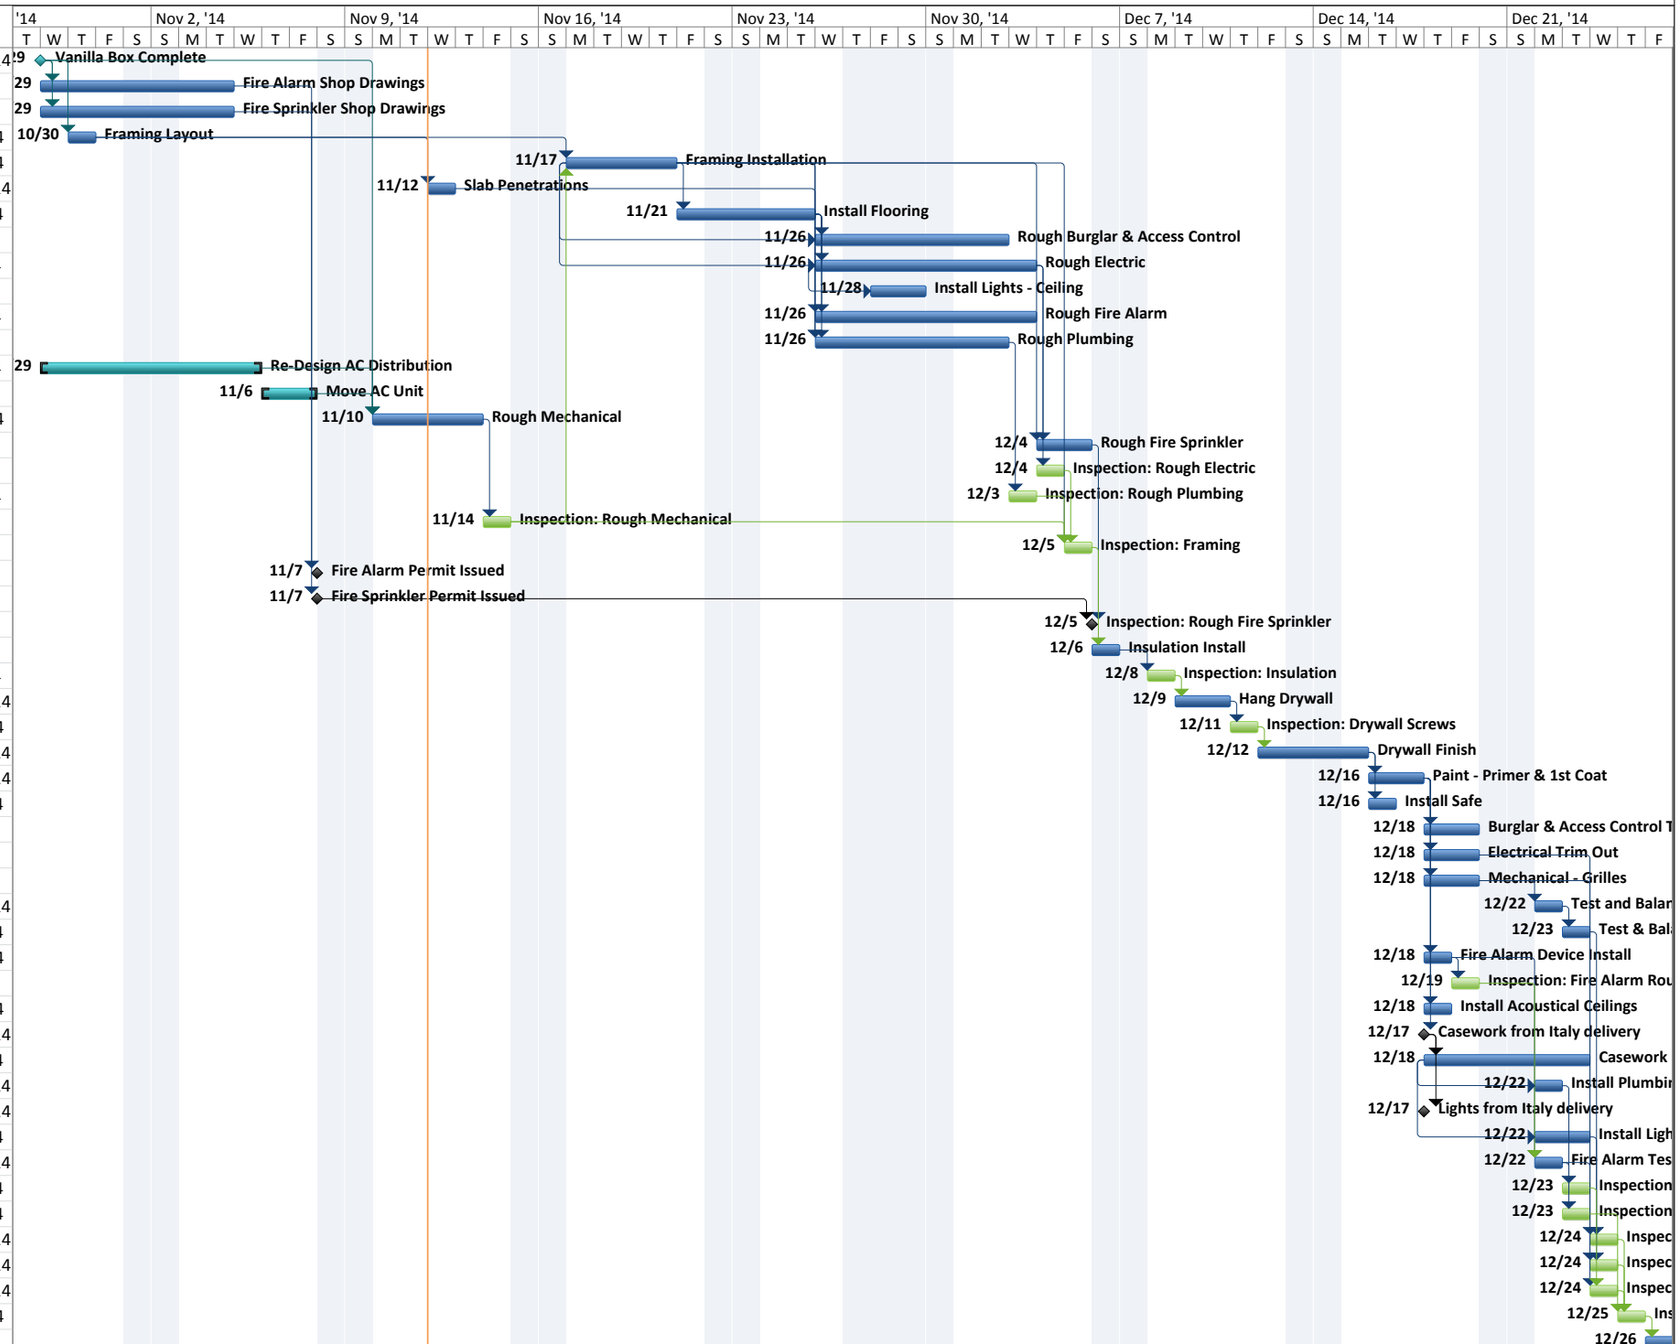
ID	Task Name	Duration	Start	Finish
1	Vanilla Box Complete	0 days	Wed 10/29/14	Wed 10/29/14
2	Fire Alarm Shop Drawings	5 days	Wed 10/29/14	Tue 11/4/14
3	Fire Sprinkler Shop Drawings	5 days	Wed 10/29/14	Tue 11/4/14
4	Framing Layout	1 day	Thu 10/30/14	Thu 10/30/14
5	Framing Installation	4 days	Mon 11/17/14	Thu 11/20/14
6	Slab Penetrations	1 day	Wed 11/12/14	Wed 11/12/14
7	Install Flooring	4 days	Fri 11/21/14	Tue 11/25/14
8	Rough Burglar & Access Control	3 days	Wed 11/26/14	Tue 12/2/14
9	Rough Electric	4 days	Wed 11/26/14	Wed 12/3/14
10	Install Lights - Ceiling	2 days	Fri 11/28/14	Sat 11/29/14
11	Rough Fire Alarm	4 days	Wed 11/26/14	Wed 12/3/14
12	Rough Plumbing	3 days	Wed 11/26/14	Tue 12/2/14
13	Re-Design AC Distribution	6 days	Wed 10/29/14	Wed 11/5/14
14	Move AC Unit	2 days	Thu 11/6/14	Fri 11/7/14
15	Rough Mechanical	4 days	Mon 11/10/14	Thu 11/13/14
16	Rough Fire Sprinkler	2 days	Thu 12/4/14	Fri 12/5/14
17	Inspection: Rough Electric	1 day	Thu 12/4/14	Thu 12/4/14
18	Inspection: Rough Plumbing	1 day	Wed 12/3/14	Wed 12/3/14
19	Inspection: Rough Mechanical	1 day	Fri 11/14/14	Fri 11/14/14
20	Inspection: Framing	1 day	Fri 12/5/14	Fri 12/5/14
21	Fire Alarm Permit Issued	0 days	Fri 11/7/14	Fri 11/7/14
22	Fire Sprinkler Permit Issued	0 days	Fri 11/7/14	Fri 11/7/14
23	Inspection: Rough Fire Sprinkler	0 days	Fri 12/5/14	Fri 12/5/14
24	Insulation Install	1 day	Sat 12/6/14	Sat 12/6/14
25	Inspection: Insulation	1 day	Mon 12/8/14	Mon 12/8/14
26	Hang Drywall	2 days	Tue 12/9/14	Wed 12/10/14
27	Inspection: Drywall Screws	1 day	Thu 12/11/14	Thu 12/11/14
28	Drywall Finish	3 days	Fri 12/12/14	Mon 12/15/14
29	Paint - Primer & 1st Coat	2 days	Tue 12/16/14	Wed 12/17/14
30	Install Safe	1 day	Tue 12/16/14	Tue 12/16/14
31	Burglar & Access Control Trim Out	2 days	Thu 12/18/14	Fri 12/19/14
32	Electrical Trim Out	2 days	Thu 12/18/14	Fri 12/19/14
33	Mechanical - Grilles	2 days	Thu 12/18/14	Fri 12/19/14
34	Test and Balance	1 day	Mon 12/22/14	Mon 12/22/14
35	Test & Balance Report Issued	1 day	Tue 12/23/14	Tue 12/23/14
36	Fire Alarm Device Install	1 day	Thu 12/18/14	Thu 12/18/14
37	Inspection: Fire Alarm Rough	1 day	Fri 12/19/14	Fri 12/19/14
38	Install Acoustical Ceilings	1 day?	Thu 12/18/14	Thu 12/18/14
39	Casework from Italy delivery	0 days	Wed 12/17/14	Wed 12/17/14
40	Casework Installation	4 days	Thu 12/18/14	Tue 12/23/14
41	Install Plumbing Fixtures	1 day	Mon 12/22/14	Mon 12/22/14
42	Lights from Italy delivery	0 days	Wed 12/17/14	Wed 12/17/14
43	Install Lights - Display Cases	2 days	Mon 12/22/14	Tue 12/23/14
44	Fire Alarm Test	1 day	Mon 12/22/14	Mon 12/22/14
45	Inspection: Final Fire Alarm	1 day	Tue 12/23/14	Tue 12/23/14
46	Inspection: Final Plumbing	1 day	Tue 12/23/14	Tue 12/23/14
47	Inspectoin: Final Electrical	1 day	Wed 12/24/14	Wed 12/24/14
48	Inspection: Final Mechanical	1 day	Wed 12/24/14	Wed 12/24/14
49	Inspection Final Fire	1 day	Wed 12/24/14	Wed 12/24/14
50	Inspection: Final Building	1 day	Thu 12/25/14	Thu 12/25/14
51	Obtain Certificate of Occupancy	1 day	Fri 12/26/14	Fri 12/26/14
