VHERNIER MIAMI AT DESIGN DISTRICT
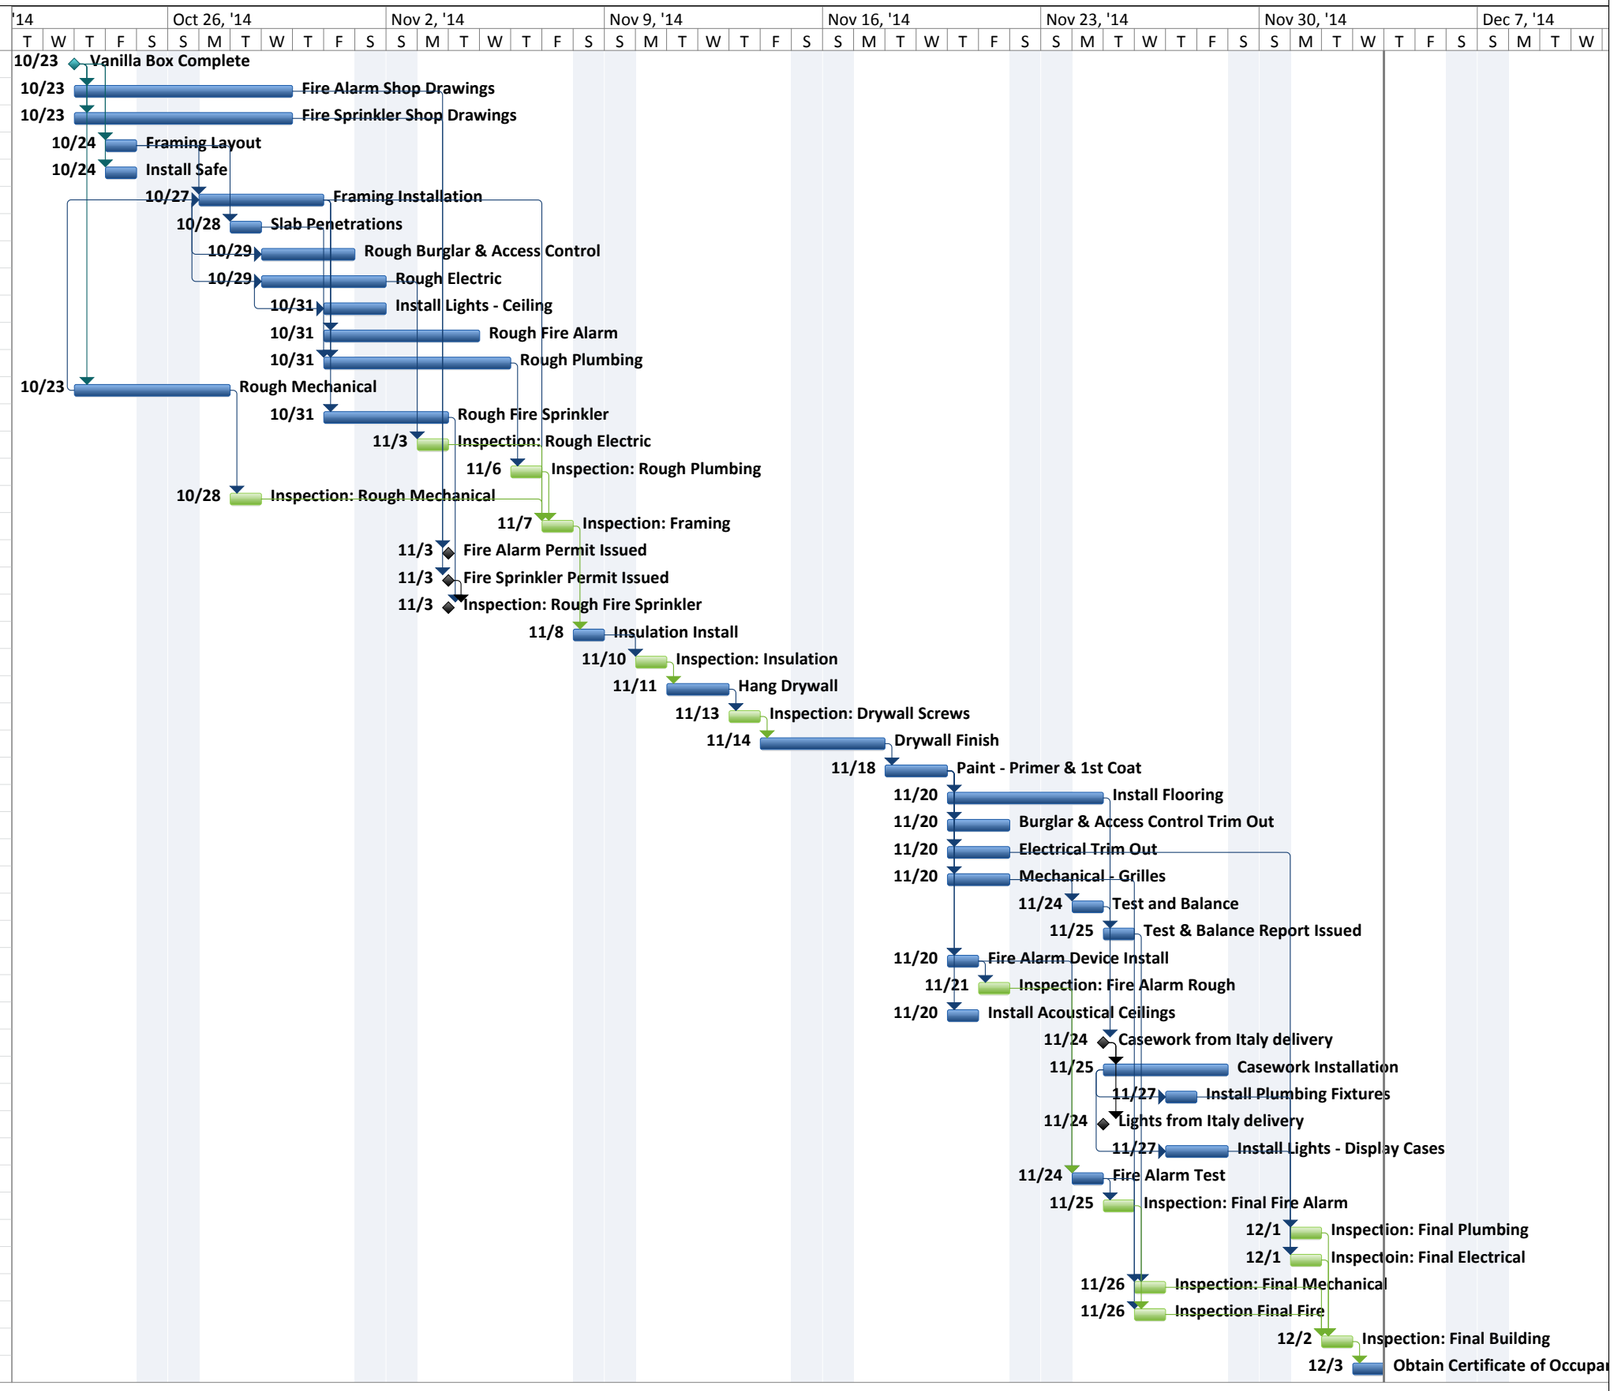
ID	Task Name	Duration	Start	Finish	Predecessors
1	Vanilla Box Complete	0 days	Thu 10/23/14	Thu 10/23/14	
2	Fire Alarm Shop Drawings	5 days	Thu 10/23/14	Wed 10/29/14	1
3	Fire Sprinkler Shop Drawings	5 days	Thu 10/23/14	Wed 10/29/14	1
4	Framing Layout	1 day	Fri 10/24/14	Fri 10/24/14	1FS+1 day
5	Install Safe	1 day	Fri 10/24/14	Fri 10/24/14	1FS+1 day
6	Framing Installation	4 days	Mon 10/27/14	Thu 10/30/14	4,13SS+3 days
7	Slab Penetrations	1 day	Tue 10/28/14	Tue 10/28/14	4FS+1 day
8	Rough Burglar & Access Control	3 days	Wed 10/29/14	Fri 10/31/14	6SS+2 days
9	Rough Electric	4 days	Wed 10/29/14	Sat 11/1/14	6SS+2 days
10	Install Lights - Ceiling	2 days	Fri 10/31/14	Sat 11/1/14	9SS+2 days
11	Rough Fire Alarm	4 days	Fri 10/31/14	Tue 11/4/14	6
12	Rough Plumbing	4 days	Fri 10/31/14	Wed 11/5/14	7,6
13	Rough Mechanical	4 days	Thu 10/23/14	Mon 10/27/14	1
14	Rough Fire Sprinkler	2 days	Fri 10/31/14	Mon 11/3/14	6
15	Inspection: Rough Electric	1 day	Mon 11/3/14	Mon 11/3/14	9
16	Inspection: Rough Plumbing	1 day	Thu 11/6/14	Thu 11/6/14	12
17	Inspection: Rough Mechanical	1 day	Tue 10/28/14	Tue 10/28/14	13
18	Inspection: Framing	1 day	Fri 11/7/14	Fri 11/7/14	6,15,16,17
19	Fire Alarm Permit Issued	0 days	Mon 11/3/14	Mon 11/3/14	2FS+3 days
20	Fire Sprinkler Permit Issued	0 days	Mon 11/3/14	Mon 11/3/14	3FS+3 days
21	Inspection: Rough Fire Sprinkler	0 days	Mon 11/3/14	Mon 11/3/14	20,14
22	Insulation Install	1 day	Sat 11/8/14	Sat 11/8/14	18
23	Inspection: Insulation	1 day	Mon 11/10/14	Mon 11/10/14	22
24	Hang Drywall	2 days	Tue 11/11/14	Wed 11/12/14	23
25	Inspection: Drywall Screws	1 day	Thu 11/13/14	Thu 11/13/14	24
26	Drywall Finish	3 days	Fri 11/14/14	Mon 11/17/14	25
27	Paint - Primer & 1st Coat	2 days	Tue 11/18/14	Wed 11/19/14	26
28	Install Flooring	4 days	Thu 11/20/14	Mon 11/24/14	27
29	Burglar & Access Control Trim Out	2 days	Thu 11/20/14	Fri 11/21/14	27
30	Electrical Trim Out	2 days	Thu 11/20/14	Fri 11/21/14	27
31	Mechanical - Grilles	2 days	Thu 11/20/14	Fri 11/21/14	27
32	Test and Balance	1 day	Mon 11/24/14	Mon 11/24/14	31
33	Test & Balance Report Issued	1 day	Tue 11/25/14	Tue 11/25/14	32
34	Fire Alarm Device Install	1 day	Thu 11/20/14	Thu 11/20/14	27
35	Inspection: Fire Alarm Rough	1 day	Fri 11/21/14	Fri 11/21/14	34
36	Install Acoustical Ceilings	1 day?	Thu 11/20/14	Thu 11/20/14	27
37	Casework from Italy delivery	0 days	Mon 11/24/14	Mon 11/24/14	28
38	Casework Installation	4 days	Tue 11/25/14	Fri 11/28/14	37
39	Install Plumbing Fixtures	1 day	Thu 11/27/14	Thu 11/27/14	38SS+2 days
40	Lights from Italy delivery	0 days	Mon 11/24/14	Mon 11/24/14	37
41	Install Lights - Display Cases	2 days	Thu 11/27/14	Fri 11/28/14	38SS+2 days
42	Fire Alarm Test	1 day	Mon 11/24/14	Mon 11/24/14	34,35
43	Inspection: Final Fire Alarm	1 day	Tue 11/25/14	Tue 11/25/14	42
44	Inspection: Final Plumbing	1 day	Mon 12/1/14	Mon 12/1/14	39
45	Inspectoin: Final Electrical	1 day	Mon 12/1/14	Mon 12/1/14	30,41
46	Inspection: Final Mechanical	1 day	Wed 11/26/14	Wed 11/26/14	31,33
47	Inspection Final Fire	1 day	Wed 11/26/14	Wed 11/26/14	42,43
48	Inspection: Final Building	1 day	Tue 12/2/14	Tue 12/2/14	47,45,44,46
49	Obtain Certificate of Occupancy	1 day	Wed 12/3/14	Wed 12/3/14	48
